


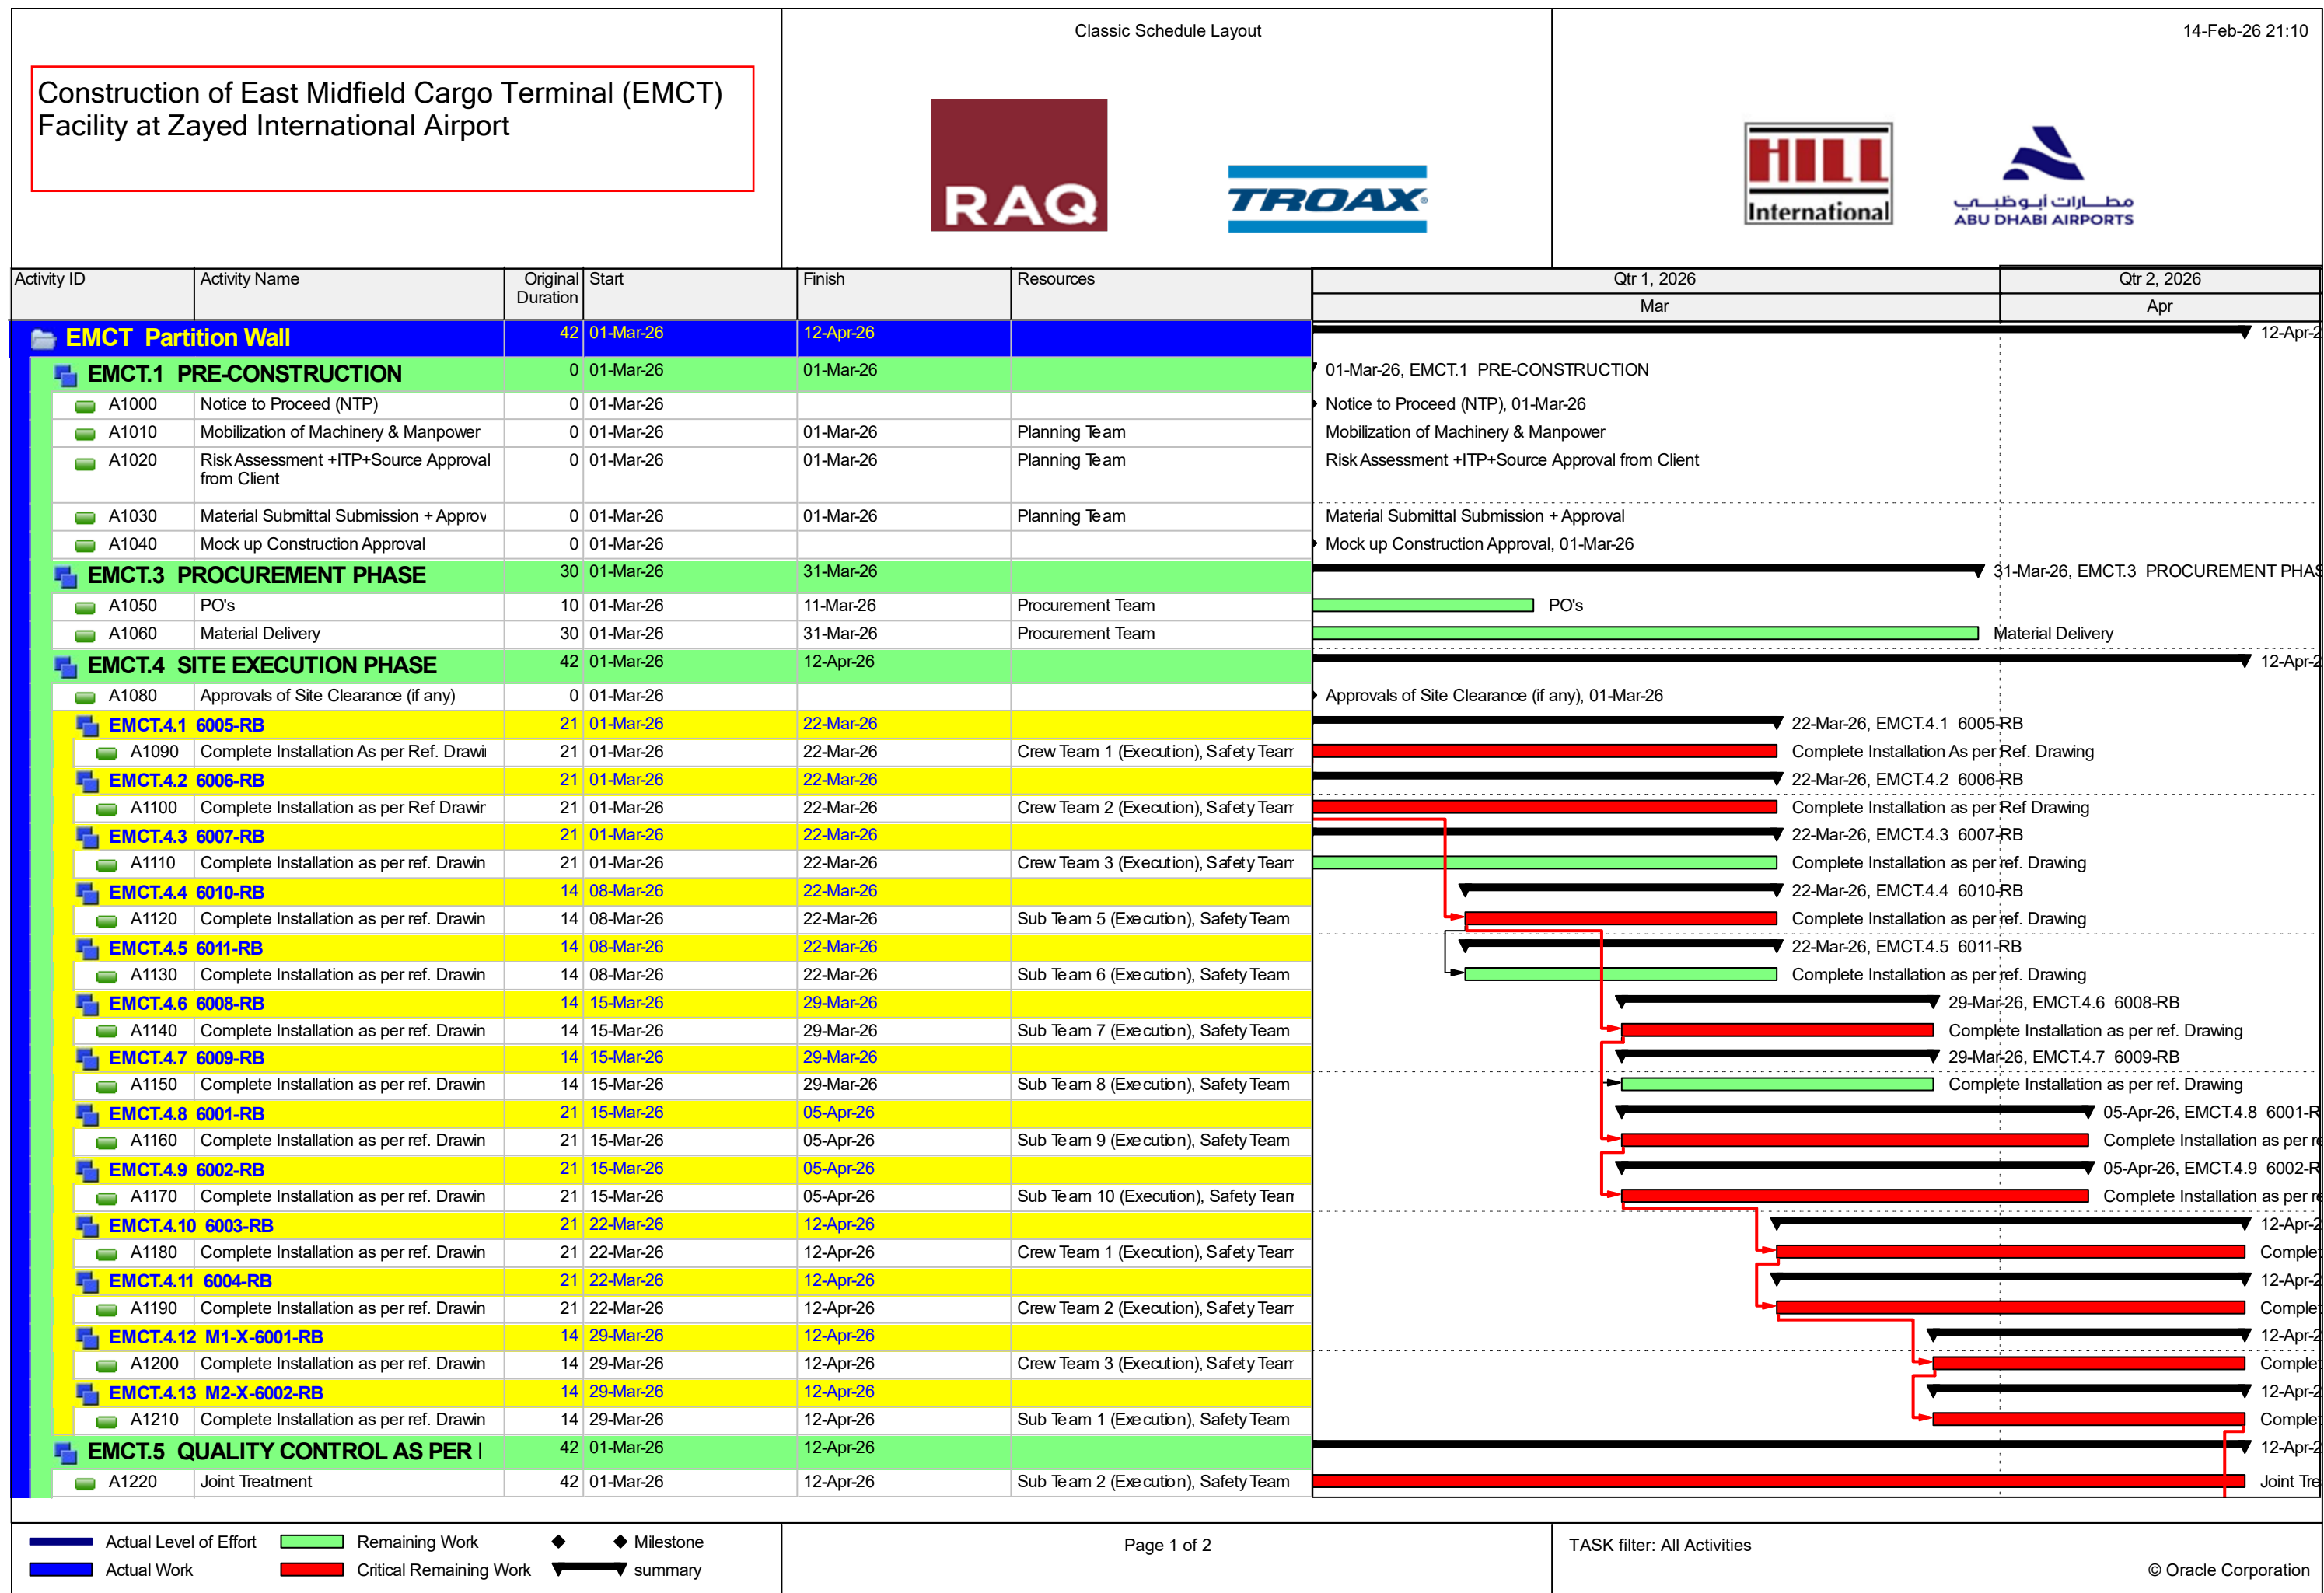

Construction of East Midfield Cargo Terminal (EMCT)
Facility at Zayed International Airport

Classic Schedule Layout

RAQ

TROAX

HILL
International

مطارات أبوظبي
ABU DHABI AIRPORTS

Activity ID	Activity Name	Original Duration	Start	Finish	Resources	Qtr 1, 2026	Qtr 2, 2026
						Mar	Apr
A1230	Snag Rectification	42	01-Mar-26	12-Apr-26	Sub Team 3 Execution, Safety Team	Snag Rectification	
A1240	Inspections + MIR	42	01-Mar-26	12-Apr-26	Sub Team 4 (Execution), Safety Team	Inspection	
EMCT.6 TESTING & HANDOVER		0	12-Apr-26	12-Apr-26		12-Apr-26	
A1250	Handing over site to client	0		12-Apr-26		Handing over	

Notes-

A. Material Supply:

Material shall be supplied within 8 weeks from the date of final color approval. Installation works will commence only after receipt of approved materials at site.

B. FFL Readiness:

Finished Floor Level (FFL) must be completed and handed over area-wise prior to commencement of installation works in the respective areas.

C. Partition Wall Marking / Installation:

Partition wall marking and installation shall be completed in the respective areas to facilitate measurement and commencement of MPS works.

THE WORK PROGRAMME IS BASED ON OPTIMISTIC APPROACH, THE SAME SHALL BE REVISED ON OCCURENCE OF ANY PHYSICAL / FINANCIAL CONSTRAINT

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

summary

Page 2 of 2

TASK filter: All Activities

© Oracle Corporation
